

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #105  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 24125
- » Total Man Hours on Project: 965963
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

### East Zone

- » Continued MEP Rough-In @ Building E.
- » Installed Paper Towel Dispensers @ Bldgs G & F.
- » Continued Painting Walls @ Buildings F & E.
- » Continued Lights and Devices @ Building E.
- » Began Spreading Top Soil @ East Zone.
- » Continued Point Up @ Building F 3rd Floor.
- » Continued Installing Irrigation Along East Spine.
- » Poured Footings For Dumpster Pad Walls.
- » Painted Exterior Doors @ Building G.
- » Continued Drywall Hanging & Finishing @ Building E.
- » Continued Punchlist @ Building G.
- » Placed Top Soil @ Bldgs. G, E & F



Bldg. G Main Lobby Light Fixtures



Building E Complex Lounge




Dumpster Wall Foundations

### SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Bldgs. B and C.
- » Continued Brick Masonry @ Bldg. C.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Roofing @ Building D.
- » Continued Glass Installation @ HUB & Building C.
- » Continued Newman Rd Intersection Roadwork.
- » Poured Sidewalks @ Newman Road Intersection.
- » Continued Window Frame Install @ Building D.
- » Continued Finishing Drywall @ Building A.
- » Continued Hanging Drywall @ Building B.
- » Continued Sidewalk and Structural Soil



Top Soil Spreading

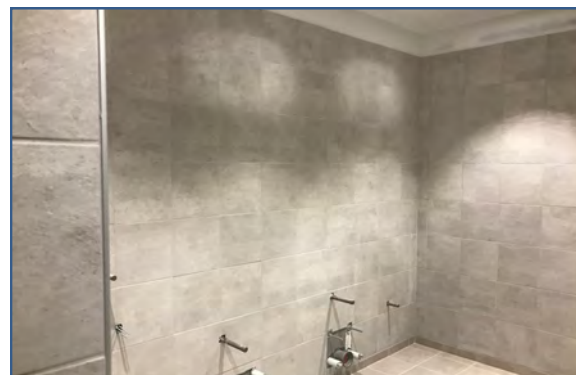

Building E Wall Tile

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #105  
Douthitt Hills Student Community, Clemson University Project  
Joe Jett



## NEXT WEEK'S ACTIVITIES

### East Zone

- » Continue Overhead Rough-In @ Buildings E.
- » Continue Finishing Drywall @ Building E.
- » Continue Painting @ Building F.
- » Continue Wall Tile @ Building F & E.
- » Continue Priming Walls @ Building E.
- » Continue Installing Lights & Devices @ Bldg. E.
- » Continue Point Up 3rd Floor @ Building F.
- » Continue Punch List @ Building G.
- » Continue Millwork @ Bldg. F
- » Continue Hardscape @ East Zone



Building B DEFS



Building D ERV Unit



Building D Window Frames

### SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ Building C.
- » Continue MEP Rough-In @ Bldgs. A, B, & HUB.
- » Continue Interior Framing & Drywall @ Bldg B.
- » Continue Roof Decking @ Building D.
- » Begin Trash Walls North of Building E.
- » Continue Framing Interior Walls @ Building C.
- » Continue Priming Walls @ Building A.
- » Continue Temp Lights @ Building D.
- » Continue Newman Road Intersection Roadwork.
- » Continue Storm Structures @ HUB & Bldg. E



HUB Sunshade Infill



Building D Waterproofing

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #105  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

## TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	40	1800	111190
American Deep Foundation	Auger Cast Piles	0	0	6166
Accessories Unlimited	Bathroom Accessories	3	120	355
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Develop-	Hardscape & Landscape	10	400	5660
Cabinets By Design	Millwork	2	80	480
Carolina Fire Protection	Sprinklers	14	700	24945
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	4	200	4370
Feltman Brothers	West - Masonry	26	1300	22285
Gainesville Mechanical	Ductwork	10	500	61919
Gill Plumbing	Plumbing	36	1800	35580
Graham Hodge	Glass	8	320	5330
Gregory Electric	Aboveground Electric	17	850	20400
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	14	700	15252
Johnson Controls	Building Controls	9	450	7235
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	44	1760	47482
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	100	3363
Labor Finders	Labor Force	12	480	44748
Metro Power	Underground Electrical	9	360	22587
Nations Roofing	Roofing	7	280	8235
Old North State Masonry	East - Masonry	0	0	28829
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	5	250	84860



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #105  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER

### CURRENT WEEK

5	Rain		6	Rain		7	Rain		8	Tstorm		9	Tstorm		10	Clear		11	Partly Cloudy	
Actual: 62°   32°	Actual: 66°   36°	Actual: 64°   46°	Actual: 71°   54°	Actual: 60°   36°	Actual: 57°   30°	Actual: 71°   43°	0.00 in	0.00 in	0.44 in	0.13 in	0.10 in	0.00 in	0.00 in	0.00 in	0.00 in	0.00 in	0.00 in	0.00 in	0.00 in	0.00 in
Average: 56°   29°	Average: 53°   31°	Average: 53°   29°	Average: 54°   29°	Average: 53°   26°	Average: 52°   28°	Average: 54°   30°	0.11 in	0.11 in	0.18 in	0.13 in	0.02 in	0.09 in	0.09 in	0.09 in	0.09 in	0.09 in	0.09 in	0.14 in	0.14 in	0.14 in

Rain Days This Week = 0


Rain Days To Date = 63

## SAFETY REVIEW LOG

### Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

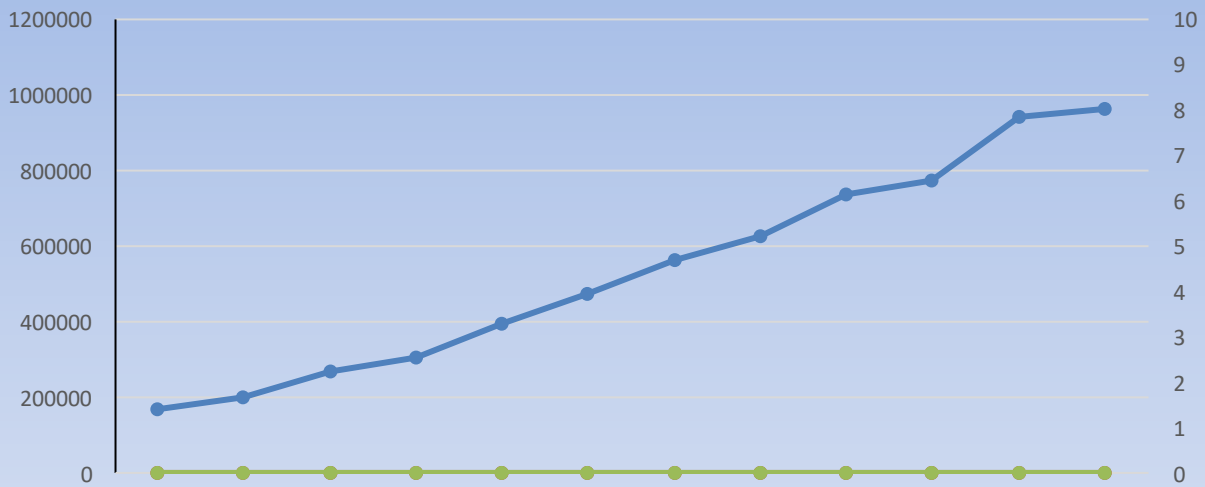

	Mar-16	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Jan-17	Feb-17
● Cumulative Man-Hours	166748	201384	268272	307534	395795	475812	563897	627462	738504	776399	941838	965963
● RCR	0	0	0	0	0	0	0	0	0	0	0	0
● DART R	0	0	0	0	0	0	0	0	0	0	0	0



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #105  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

