

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #108  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 23271
- » Total Man Hours on Project: 1035609
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0






## CURRENT CONSTRUCTION ACTIVITIES

### East Zone

- » Continued Painting Walls @ Building F.
- » Continued Hanging ACT Grid @ Building E.
- » Installed Wood Slat Walls @ Bldgs. G & F.
- » Poured Fire Lane @ East Spine.
- » Continued Punch List @ Building G 4th Floor.
- » Continued Drywall Hanging & Finishing @ Building E.
- » Continued Fire Alarm Testing @ Building G.
- » Continued Overhead Inspections @ Building G.
- » Continued Wall Tile in Buildings F & E.
- » Installed Millwork in Graduate Apartments in Buildings G & F.



Emergency Phone @ East Spine

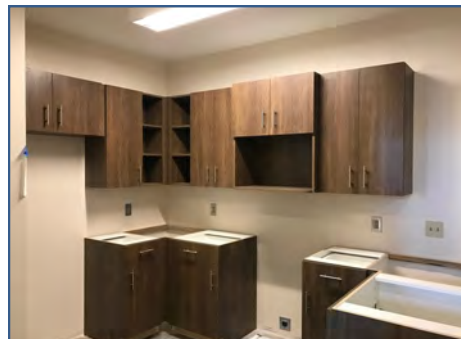

Building F Graduate Apartment Millwork



Building F Exterior Door Hardware Installed

### SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Bldgs. B and C.
- » Continued Installing Gutters @ Bldg. D.
- » Continued Brick Masonry @ Bldg. D.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. C.
- » Continued Irrigation Install @ East Zone
- » Paved Decel Lane and Center Turning Lane @ Newman Rd.
- » Continued Frame Install @ Building D.
- » Continue Hanging Drywall @ Building B.
- » Poured Curb and Gutter North of Building E.
- » Continued DEIFS @ Bldgs. B & C.
- » Continued Sunshade Infill @ HUB.



Fire Lane Between Bldgs. E & F



Fire Lane & Building E Breezeway





## NEXT WEEK'S ACTIVITIES

### East Zone

- » Begin Overhead Inspection @ Building F.
- » Continue Finishing Drywall @ Building E.
- » Continue Painting @ Building E.
- » Continue Wall Tile @ Buildings F & E.
- » Continue Installing Lights & Devices @ Bldg. E.
- » Continue Trim Out @ Building F 4th Floor.
- » Punch Building F 3rd & 4th Floor.
- » Continue ACT Grid @ Building E.
- » Begin 1st Floor Lobby Tile @ Building F.
- » Continue Punch List @ Building G 3rd Floor.



Building C Overhead Rough-In



Louvers @ HUB



Building B Duct Insulation

### SITE, HUB, & WEST ZONE

- » Continue Brick Masonry @ Buildings C & D
- » Continue MEP Rough-In @ Bldgs. A, B, & HUB.
- » Continue Hanging Drywall @ Bldg. B.
- » Continue Roofing @ Building D.
- » Continue Framing Walls @ Buildings C& D.
- » Continue Painting Walls @ Building A.
- » Continue Hwy 93 Roadwork.
- » Continue Gutters @ Building D.
- » Continue Loading Dock @ HUB.
- » Continue DEIFS @ Bldgs. B & C.
- » Continue Curb & Gutter @ East Zone.



Newman Rd. Intersection Center Lane



Decel Lane @ Newman Rd.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #108  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

## TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	40	1800	116590
American Deep Foundation	Auger Cast Piles	0	0	6166
Accessories Unlimited	Bathroom Accessories	0	0	435
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Develop-	Hardscape & Landscape	8	320	6700
Cabinets By Design	Millwork	5	200	760
Carolina Fire Protection	Sprinklers	15	750	26745
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	4	200	4970
Feltman Brothers	West - Masonry	25	1250	25835
Gainesville Mechanical	Ductwork	8	400	62969
Gill Plumbing	Plumbing	38	1900	41180
Graham Hodge	Glass	6	240	5890
Gregory Electric	Aboveground Electric	10	500	22500
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	14	700	17352
Johnson Controls	Building Controls	9	450	8585
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	40	1600	52282
King Asphalt	Asphalt	12	96	4285
Kone	Elevators	2	100	3663
Labor Finders	Labor Force	12	480	46188
Metro Power	Underground Electrical	9	360	23667
Nations Roofing	Roofing	11	440	9235
Old North State Masonry	East - Masonry	0	0	28859
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	5	250	85610



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #108  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## MANPOWER CONTINUED

### TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Pro Door	Doors & Hardware	9	450	2950
Pyramid Masonry	Hub—Masonry	6	240	13080
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	8	360	63223
Rival Construction Inc.	Concrete	6	240	41256
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	70	3360	142092
Sentential Maintenance	Construction Cleaning	12	660	3465
Silt Fence Installation	Site Erosion Control	0	0	1031
Simplex	Controls	9	450	5580
Southern Mechanical Inc.	Electrical/Plumbing	81	3645	87945
Specialty Finishes	Painting	16	720	6800
Steel Toe	Labor Force	10	400	14815
TG Welding	Misc. Steel	7	280	3300
Tree South	Arborist	0	0	2077
Upstate Curb	Curb and Gutter	6	180	1224
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	5	250	4054
<b>Total</b>		<b>518</b>	<b>23271</b>	<b>1035609</b>




# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #108  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER

### CURRENT WEEK




## SAFETY REVIEW LOG

### Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

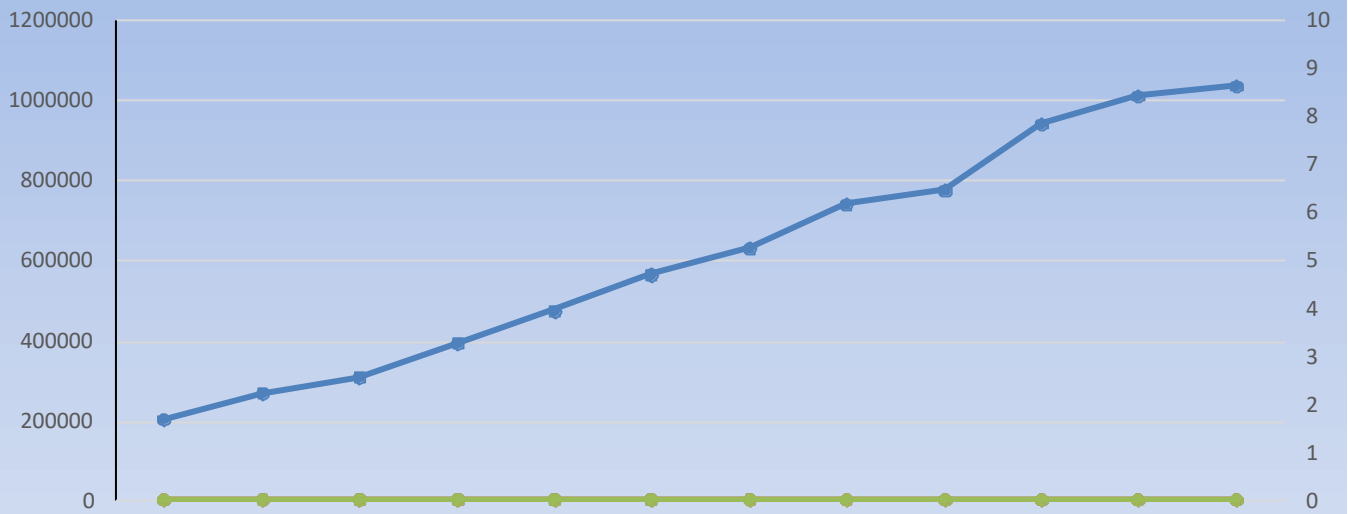

	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Jan-17	Feb-17	Mar-17
Cumulative Man-Hours	201384	268272	307534	395795	475812	563897	627462	738504	776399	941838	1012338	1035609
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART	0	0	0	0	0	0	0	0	0	0	0	0



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #108  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

### Douthit Hills Workforce

