



HOLDER CONSTRUCTION COMPANY

Superintendent's Weekly Activity Report #114
Douthit Hills Student Community, Clemson University Project
Joe Jett





CURRENT CONSTRUCTION ACTIVITIES

EAST ZONE & SITE

- Continued Finishing Drywall @ Building E.
- Punched Building E 1st & 2nd Floor.
- Continued Painting @ Bldg. E.
- Continued Wall Tile @ Bldg. E.
- Continued Installing Lights & Devices @ Bldg. E.
- Continued ACT Grid @ Bldg. E.
- Continued Punch List in Building G & F.
- Continued Installing Carpet in Building G.
- Completed Screen Walls North of Bldg. E.
- Continued T&B @ Building G.
- Continued Final Painting @ Building G 4th Floor.
- Continued HWY 93 Rd Work.



Building E Complex Lounge- Wood Feature Wall

WEST ZONE & HUB

- Continued Framing @ Bldg. B and C.
- Continued West Elevator @ Building B.
- Continued MEP Rough-In @ Bldgs. A, B & HUB.
- Continued DEIFS @ Bldgs. B & C.
- Continued Painting @ Bldg. A.
- Continued Door Hardware @ Building A.
- Continued Hanging Drywall @ Bldg. B.
- Continued Interior Framing @ HUB.
- Continued Shingles @ Building D.
- Continued Sundhade Infill @ HUB.
- Continued Installing Lights & Devices @ Building A.



Building A Wood Doors and Hardware



NEXT WEEK'S ACTIVITIES

EAST ZONE & SITE

- Continue Finishing Drywall @ Building E.
- Continue Painting @ Building E.
- Continue Wall Tile @ Building E.
- Punch Building E 3rd Floor.
- Continue Installing Lights & Devices @ Bldg. E.
- Continue ACT Grid @ Building E.
- Drop Acustical Tile @ Building F 4th Floor.
- Continue Carpet @ Building G 1st Floor.
- Begin Carpet @ Building F 4th Floor.
- Continue HWY 93 Roadwork.



HUB Interior Framing – Elevator Lobby

WEST ZONE & HUB

- Continue MEP Rough-In @ Bldgs. A, B, C & HUB.
- Continue Hanging Drywall @ Bldgs. B & C.
- Continue Framing Walls @ Buildings C & D.
- Continue Painting Walls @ Building A.
- Continue DEIFS @ Bldgs. B & C.
- Continue Glass Installation @ Building D.
- Continue Interior Framing @ HUB.
- Continue Door Hardware @ Building A.
- Continue Rough-In @ HUB 1st Floor.



Firelane North of Building F



WEATHER

CURRENT WEEK

10 Clear Actual: 79° 51° 0.00 in Average: 70° 43° 0.13 in	11 Clear Actual: 81° 55° 0.00 in Average: 70° 43° 0.04 in	12 Tstorm Actual: 81° 57° 0.00 in Average: 73° 44° 0.09 in	13 Clear Forecast: 82° 59° 0.0 in Average: 72° 47° 0.22 in	14 Clear Forecast: 83° 62° 0.0 in Average: 72° 48° 0.16 in
--	--	---	---	---


Rain Days This Week = 0

Rain Days to Date = 67



MANPOWER

TOTAL PROJECT LABOR

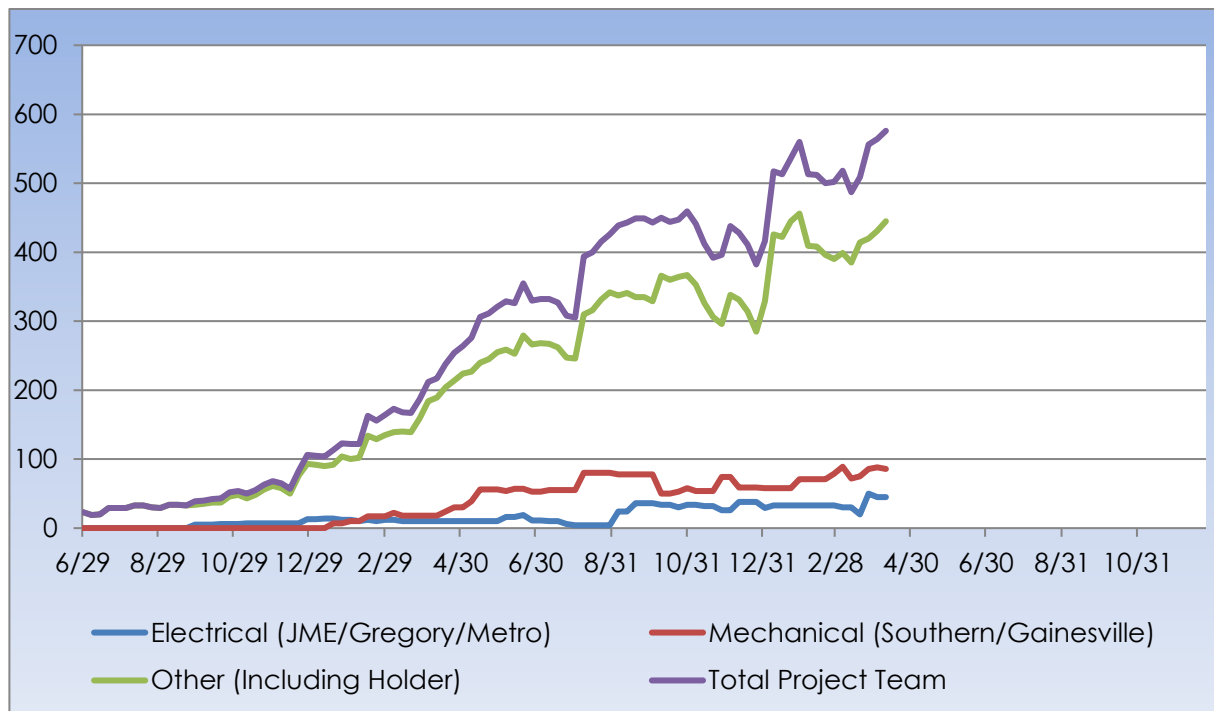



MANPOWER

TOTAL PROJECT LABOR

TRADE CONTRACTORS ON-SITE		
Subcontractor	Trade	Number of Employees
Holder Construction Company	General Contractor	35
Accessories Unlimited	Accessories	4
Brightview Landscape Development	Hardscape & Landscape	12
Cabinets By Design	Millwork	9
Carolina Fire Protection	Sprinklers	13
Elite Flooring	Tile	5
Feltman Brothers	Masonry - West	17
First Choice Glass	Glazing	6
Gainesville Mechanical	Mechanical	6
Gill Plumbing	Plumbing	44
Graham Hodge	Glazing - HUB	3
Gregory Electric	Electrical - HUB	7
Johnson Controls	Controls	9
Johnsons Modern Electric	Electrical	34
King Asphalt	Asphalt	7
Kone	Elevators	2
Labor Finders	Labor Force	14
Metro Power	Sitework Electrical	4
Nations Roofing	Roofing	10
Palmetto Waterproofing	Waterproofing	4
Precision	Concrete	6
Professional Door	Doors & Hardware	3
Pyramid Masonry	Masonry - HUB	1
Reeves Young	Site Grading & Utilities	23
Rival Construction Inc.	Concrete	2
Sears Contract	Drywall/Metal Trusses	170
Sentential Maintenance	Construction Cleaning	12
Simplex	Controls	2
Southern Mechanical Inc.	Mechanical/Plumbing	80
Specialty Finishes	Painting	17
Steel Toe	Labor Force	6
TG Welding	Misc. Steel	8
Tree South	Arborist	1
TOTAL		576



SAFETY REPORT

- Total Man Hours Worked This Week: 27,430
- Total Man Hours on Project: 1,185,848
- Crafts On Project This Week: 32
- OSHA Recordable Rate: 4.24



INSPECTIONS/TESTING REPORT

- BLE – Above Ceiling Inspection – Building F 2nd, 3rd, & 4th Floor Scheduled for next week
- CC&I – Above Ceiling Inspection – Building B
- CC&I – In-wall Rough-in Inspection – Building C
- BLE – Soil Compaction & Concrete Testing



ENVIRONMENTAL REPORT

- Pursuing LEED Silver Certification
