



HOLDER CONSTRUCTION COMPANY

Superintendent's Weekly Activity Report #115
Douthit Hills Student Community, Clemson University Project
Joe Jett





CURRENT CONSTRUCTION ACTIVITIES

EAST ZONE & SITE

- Continued Finishing Drywall @ Building E.
- Punched Building E 3rd Floor Rooms.
- Continued Painting Stairwells @ Bldg. E.
- Continued Wall Tile @ Bldg. E.
- Dropped Acustical Tile @ Building F 4th & 3rd Floor.
- Continued Punch List in Building G & F.
- Continued Installing Carpet in Building G.
- Poured Firelane N of Building F..
- Begin installing SOD @ East Zone.
- Continued Final Painting @ Building G 2nd Floor.
- Paved Cherry Road Interseption.
- Installed Traffic Poles and Signals @ Cherry Rd and Newman Rd Intersection.



East Zone SOD

WEST ZONE & HUB

- Continued Framing @ Bldg. B, C, & D.
- Continued West Elevator @ Building B.
- Continued MEP Rough-In @ Bldgs. A, B & HUB.
- Continued DEIFS @ Bldgs. B & C.
- Continued Painting @ Bldg. A.
- Continued Door Hardware @ Building A.
- Continued Hanging Drywall @ Bldg. B & HUB.
- Continued Interior Framing @ HUB.
- Continued Sundhade Infill @ HUB.
- Continued In Wall Rough-In @ Building D.



HUB First Floor Buildout



NEXT WEEK'S ACTIVITIES

EAST ZONE & SITE

- Continue Painting @ Building E.
- Begin Carpet @ Building F.
- Continue Wall Tile @ Building E.
- Begin Lobby Floor Tile @ Building E.
- Continue Installing Lights & Devices @ Bldg. E.
- Continue ACT Grid @ Building E.
- Drop Acustical Tile @ Building F 2nd Floor
- Continue HWY 93 Roadwork.
- Continue SOD @ East Zone.
- Continue Frelane N. of Building F.



West Zone

WEST ZONE & HUB

- Continue MEP Rough-In @ Bldgs. B, C & D.
- Continue Hanging Drywall @ Bldgs. B, C & HUB.
- Continue Framing Walls @ Buildings C & D.
- Continue Painting Walls @ Building A.
- Continue DEIFS @ Bldgs. B & C.
- Continue in wall rough in @ Bldg D.
- Continue Interior Framing @ HUB.
- Continue Rough-In @ HUB 1st Floor
- .Continue Fire Protection R/I @ HUB 2nd Floor.



Cherry Rd Intersection



WEATHER

CURRENT WEEK

17 Tstorm Actual: 86° 59° 1.15 in Average: 72° 46° 0.07 in	18 Rain Actual: 71° 64° 0.17 in Average: 74° 47° 0.12 in	19 Rain Actual: 69° 60° 0.43 in Average: 74° 49° 0.12 in	20 Fog Actual: 82° 59° 0.00 in Average: 74° 47° 0.09 in	21 Rain Actual: 87° 63° 0.00 in Average: 74° 48° 0.08 in
---	---	---	--	---


Rain Days This Week = 2

Rain Days to Date = 69



MANPOWER

TOTAL PROJECT LABOR

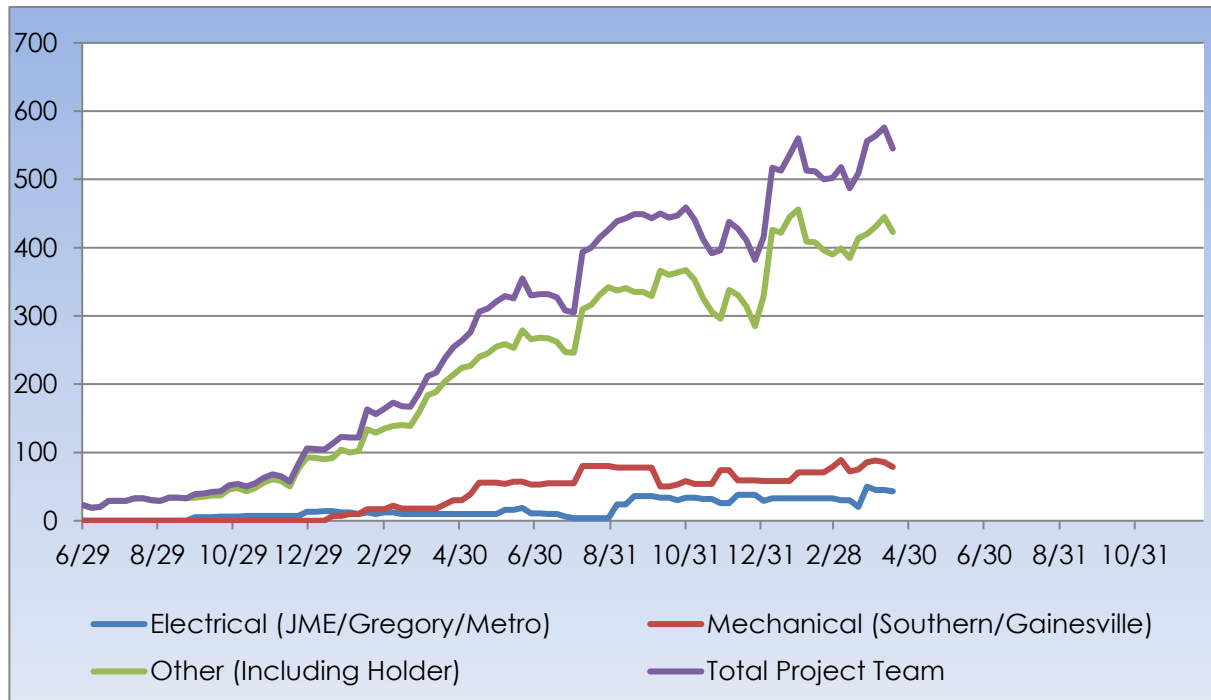



MANPOWER

TOTAL PROJECT LABOR

TRADE CONTRACTORS ON-SITE		
Subcontractor	Trade	Number of Employees
Holder Construction Company	General Contractor	35
Accessories Unlimited	Accessories	4
Brightview Landscape Development	Hardscape & Landscape	12
Cabinets By Design	Millwork	9
Carolina Fire Protection	Sprinklers	13
Elite Flooring	Tile	5
Feltman Brothers	Masonry - West	17
First Choice Glass	Glazing	6
Gainesville Mechanical	Mechanical	6
Gill Plumbing	Plumbing	44
Graham Hodge	Glazing - HUB	3
Gregory Electric	Electrical - HUB	7
Johnson Controls	Controls	9
Johnsons Modern Electric	Electrical	34
King Asphalt	Asphalt	7
Kone	Elevators	2
Labor Finders	Labor Force	14
Metro Power	Sitework Electrical	4
Nations Roofing	Roofing	10
Palmetto Waterproofing	Waterproofing	4
Precision	Concrete	6
Professional Door	Doors & Hardware	3
Pyramid Masonry	Masonry - HUB	1
Reeves Young	Site Grading & Utilities	23
Rival Construction Inc.	Concrete	2
Sears Contract	Drywall/Metal Trusses	170
Sentential Maintenance	Construction Cleaning	12
Simplex	Controls	2
Southern Mechanical Inc.	Mechanical/Plumbing	80
Specialty Finishes	Painting	17
Steel Toe	Labor Force	6
TG Welding	Misc. Steel	8
Tree South	Arborist	1
TOTAL		576



SAFETY REPORT

- Total Man Hours Worked This Week: 25,830
- Total Man Hours on Project: 1,211,678
- Crafts On Project This Week: 32
- OSHA Recordable Rate: 4.24



INSPECTIONS/TESTING REPORT

- BLE –Passed Above Ceiling Inspection – Building F 4th and 3rd
- BLE - Above Ceiling Inspection 2nd Floor.
- CC&I – Stairwell Above Ceiling Inspection – Building A
- CC&I – Above Ceiling Inspection – Building C
- CC&I – Telcom_Electrical Rooms MEP In-wall Inspections – Building D
- BLE – Soil Compaction & Concrete Testing



ENVIRONMENTAL REPORT

- Pursuing LEED Silver Certification
