HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #66
Douthit Hills Student Community, Clemson University Project
Joe Jett

SAFETY

- Total Man Hours Worked This Week: 13206
- Total Man Hours on Project: 226241
- Crafts On Project This Week: 16
- OSHA Recordable Rate: 0

CURRENT CONSTRUCTION ACTIVITIES

East Zone

- Continued Window Frame Installation @ Building E.
- Continued Brick Masonry @ Building G.
- Continued Mechanical Rough-In @ Building F.
- Continued Installing Fascia@ Building G.
- Began Gutters @ Building G.
- Poured Building E Sequence 2 Slab On Grade.
- Continued Electrical Rough-In @ Building F.
- Continued Sprinklers @ Building G .
- Continued Stair Rails @ Building F.
- Continued Brick Angle @ Building E.

Bldg. G Showers

Bldg. E Load Bearing Walls

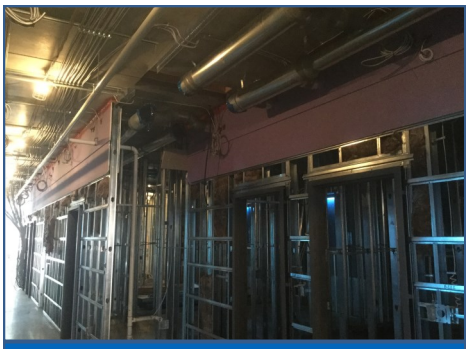

Bldg. F Overhead Rough-In

SITE, HUB, & WEST ZONE

- Continued Auger Cast Piles @ Building B.
- Continued Foundation Drains and Backfill @ Building B.
- Began Excavation For Weir Inlet on Storm Line 10.
- Continued CIP Walls @ Building B.
- Continued Precast @ Building A.
- Continued Stem Walls @ Building B.
- Poured Inverts @ East Parking Lot.
- Continued Excavation For Underground Detention System.

CIP Wall Forms and Reinforcing @ HUB

Reinforcing Steel @ HUB Elevated Slab 2A

NEXT WEEK'S ACTIVITIES

EAST ZONE

- Continue Overhead Rough-In @ Building G.
- Continue Brick @ Building G.
- Continue Stair Rails @ Building F.
- Continue Temporary Power Wiring @ Building E.
- Continue Brick Angle @ Building E.
- Continue Glazing @ Building E.
- Pour Areaway Slab @ Building E.

West Zone

Building B Backfill and Foundation Drains

SITE, HUB, & WEST ZONE

- Continue Precast @ Building A.
- Continue CIP Walls @ Building B.
- Continue Auger Cast Piles @ Building B.
- Pour Elevated Deck 2A @ HUB.
- Continue Forming HUB Elevated Deck 2B and 2C.
- Install Weir Inlet @ Storm Line 10.

MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	33	1320	47440
American Deep Foundation	Auger cast piles	9	360	5310
Baker Roofing	Sheathing and Shingles	6	250	3498
Carolina Fire Protection	Sprinklers	5	300	1050
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	480	9870
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	24	1344	6636
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	200	2536
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	12	660	4024
King Asphalt	Asphalt	0	0	2264
Labor Finders	Labor Force	9	450	20308
Metro Power	Underground Electrical	10	392	12543
Old North State Masonry	Masonry	22	1000	4560
Osteen	Chill Water pipe	0	0	2066
Precision	Concrete	60	3000	34720
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	600	39270
Rival Construction Inc.	Concrete	21	1050	5931
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	23	1040	8606
Silt Fence Installation	Site Erosion Control	0	0	999
Southern Mechanical Inc.	Electrical/Plumbing	15	600	5300
Tree South	Arborist	0	0	1431
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	5	160	474
Total		**285**	**13206**	**226241**

WEATHER

CURRENT WEEK

8 Clear	9 Scattered Clouds	10 Scattered Clouds	11 Tstorm	12 Tstorm	13 Scattered Clouds	14 Partly Cloudy
Actual: 89° | 64°	Actual: 84° | 63°	Actual: 86° | 64°	Actual: 84° | 64°	Actual: 88° | 66°	Forecast: 84° | 57°	Forecast: 84° | 52°
0.00 in	0.00 in	0.00 in	0.00 in	0.20 in	0.0 in	0.0 in
Average: 76° | 52°	Average: 75° | 52°	Average: 75° | 51°	Average: 76° | 52°	Average: 79° | 54°	Average: 80° | 56°	Average: 80° | 56°
0.23 in	0.15 in	0.16 in	0.09 in	0.12 in	0.20 in	0.17 in

Rain Days This Week = 1 Rain Days To Date = 48

SAFETY REVIEW LOG

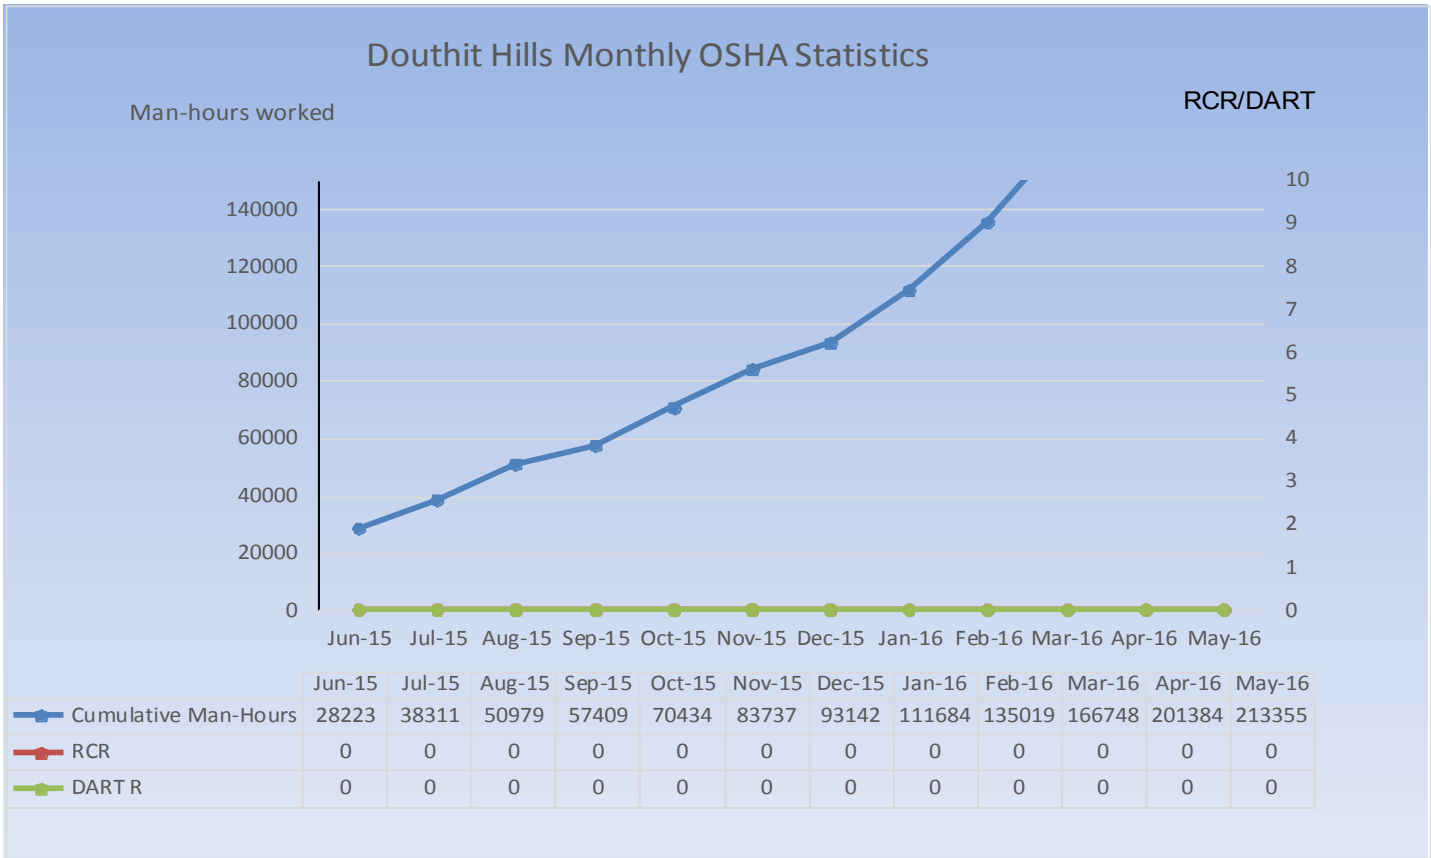

	Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16
Cumulative Man-Hours	28223	38311	50979	57409	70434	83737	93142	111684	135019	166748	201384	213355
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART R	0	0	0	0	0	0	0	0	0	0	0	0
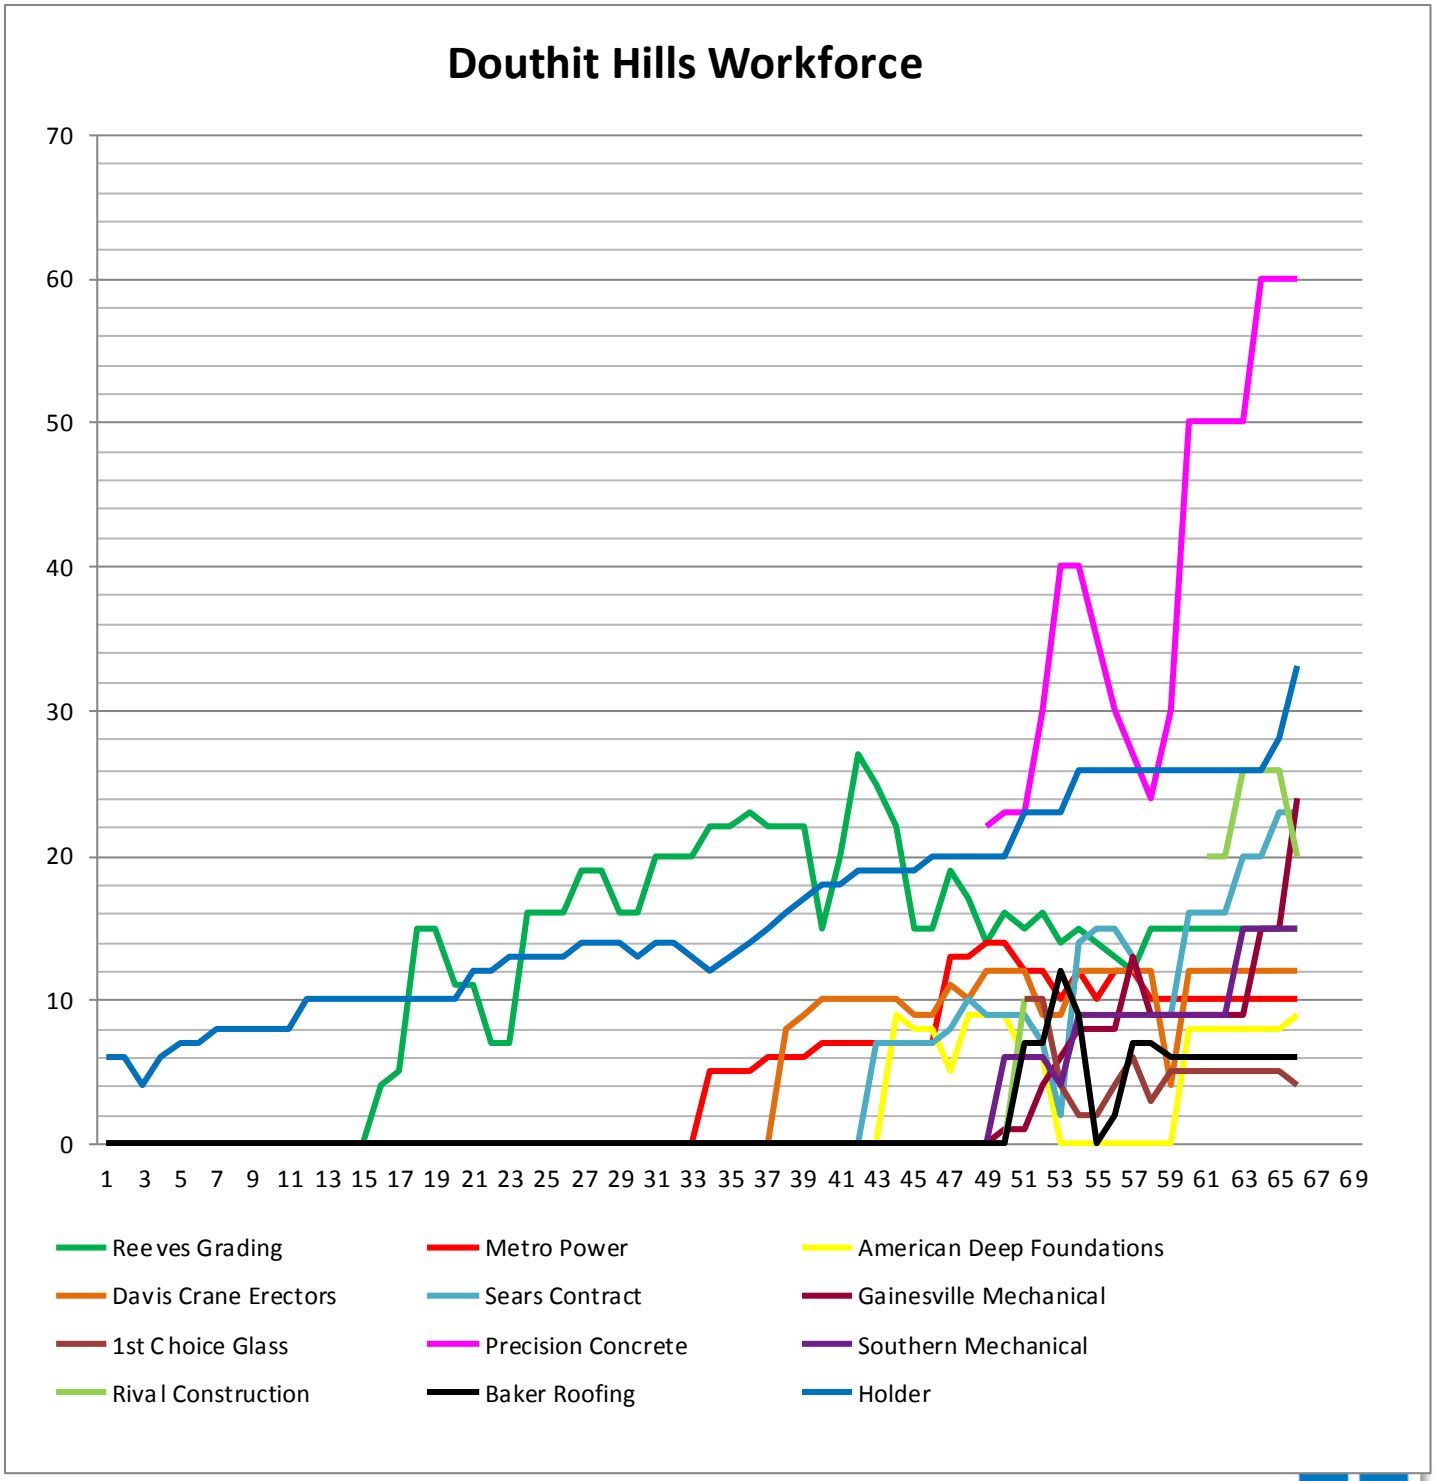
MANPOWER CHART
