SAFETY

- Total Man Hours Worked This Week: 16627
- Total Man Hours on Project: 307534
- Crafts On Project This Week: 18
- OSHA Recordable Rate: 0

CURRENT CONSTRUCTION ACTIVITIES

East Zone

- Continued Brick @ Building F.
- Continued Cleaning Brick @ Building G.
- Continued Elevators @ Building G.
- Began Brick @ Building E.
- Continued Mechanical Rough-In @ Building F.
- Continued Gutters @ Building F.
- Continued Electrical Rough-In @ Building F.
- Continued Sprinklers @ Building G & F.
- Continued Roofing @ Building E.
- Continued Setting Showers @ Building G and F.
- Continued Hanging & Finishing Drywall @ Building G.
- Continue Sanitary Rough-in @ Building E.

Bldg. G Equipment Room

Bldg. E Brick

Bldg. F Ductwork

SITE, HUB, & WEST ZONE

- Began Precast @ Building B.
- Poured 5th Floor Topping Slab @ Building A.
- Continued Excavation and Pouring Building C Foundations.
- Continued Forming and Pouring Columns @ HUB.
- Poured Elevated Deck 3A.
- Poured CIP Walls @ Building C.
- Continued Topping Slab Rough-In @ Building A.
- Continued Underground Electrical @ HUB.
- Pour Mechanical Room SOG @ HUB.

HUB Elevated Deck 3A

Mechanical Room SOG

NEXT WEEK'S ACTIVITIES

East Zone

- Continue Setting Showers @ Building G and F.
- Continue Hanging and Finishing Drywall @ Building G.
- Continued Setting Showers @ Building G and F.
- Continued Hanging & Finishing Drywall @ Building G.
- Continue Sanitary Rough-in @ Building E.
- Continue Overhead Rough-In @ Buildings G & F.
- Continue Brick @ Buildings E & F.
- Continue Glazing @ Building E.
- Continue Elevators @ Building G.
- Continue Sprinklers @ Building F.

Bldg. A 5th Floor Topping Slab

Bldg. B Precast

Bldg. C Foundations

SITE, HUB, & WEST ZONE

- Pour HUB Elevated Deck 3B.
- Continue Excavation For Underground Detention System.
- Begin Backfill & Foundation Drains @ HUB.
- Tie-In 36" and 24" Chiller Lines to HUB.
- Continue Excavation and Pouring Foundations @ Building C.
- Continue CIP Walls @ Building C.
- Continue Sanitary Lines @ HUB.
- Continue Underground Electrical @ HUB.

Building A 5th Floor Topping Slab

Building A Transformer

MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	37	1480	55720
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	8	400	5234
Carolina Fire Protection	Sprinklers	6	300	2790
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	12210
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	36	1872	15884
Gregory Electric	Aboveground Electric	6	260	1020
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	160	3232
Johnson Controls	Building Controls	3	120	720
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	14	620	7192
King Asphalt	Asphalt	0	0	2329
Kone	Elevators	2	80	320
Labor Finders	Labor Force	13	585	23288
Metro Power	Underground Electrical	19	780	15395
Old North State Masonry	Masonry	22	880	9360
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	60	2400	48720
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	16	832	43806
Rival Construction Inc.	Concrete	32	2310	15501
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	30	1350	13972
Silt Fence Installation	Site Erosion Control	2	8	1031
Southern Mechanical Inc.	Electrical/Plumbing	23	1200	10890
Steel Toe	Labor Force	6	270	4190
Tree South	Arborist	0	0	1431

MANPOWER CONTINED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	4	120	1184
Total		**355**	**16627**	**311134**

WEATHER

CURRENT WEEK

19	20	21	22	23	24	25
Scattered Clouds	Clear	Scattered Clouds	Scattered Clouds	Scattered Clouds	Clear	Clear
Actual: 86° | 68°	Actual: 91° | 64°	Actual: 97° | 69°	Actual: 99° | 75°	Actual: 98° | 77°	Actual: 99° | 80°	Forecast: 98° | 74°
0.00 in	0.00 in	0.00 in	0.00 in	0.00 in	0.00 in	0.0 in
Average: 86° | 65°	Average: 86° | 64°	Average: 87° | 65°	Average: 87° | 64°	Average: 87° | 65°	Average: 88° | 64°	Average: 88° | 65°
0.13 in	0.25 in	0.14 in	0.07 in	0.10 in	0.07 in	0.08 in

Rain Days This Week = 0 Rain Days To Date = 50

SAFETY REVIEW LOG

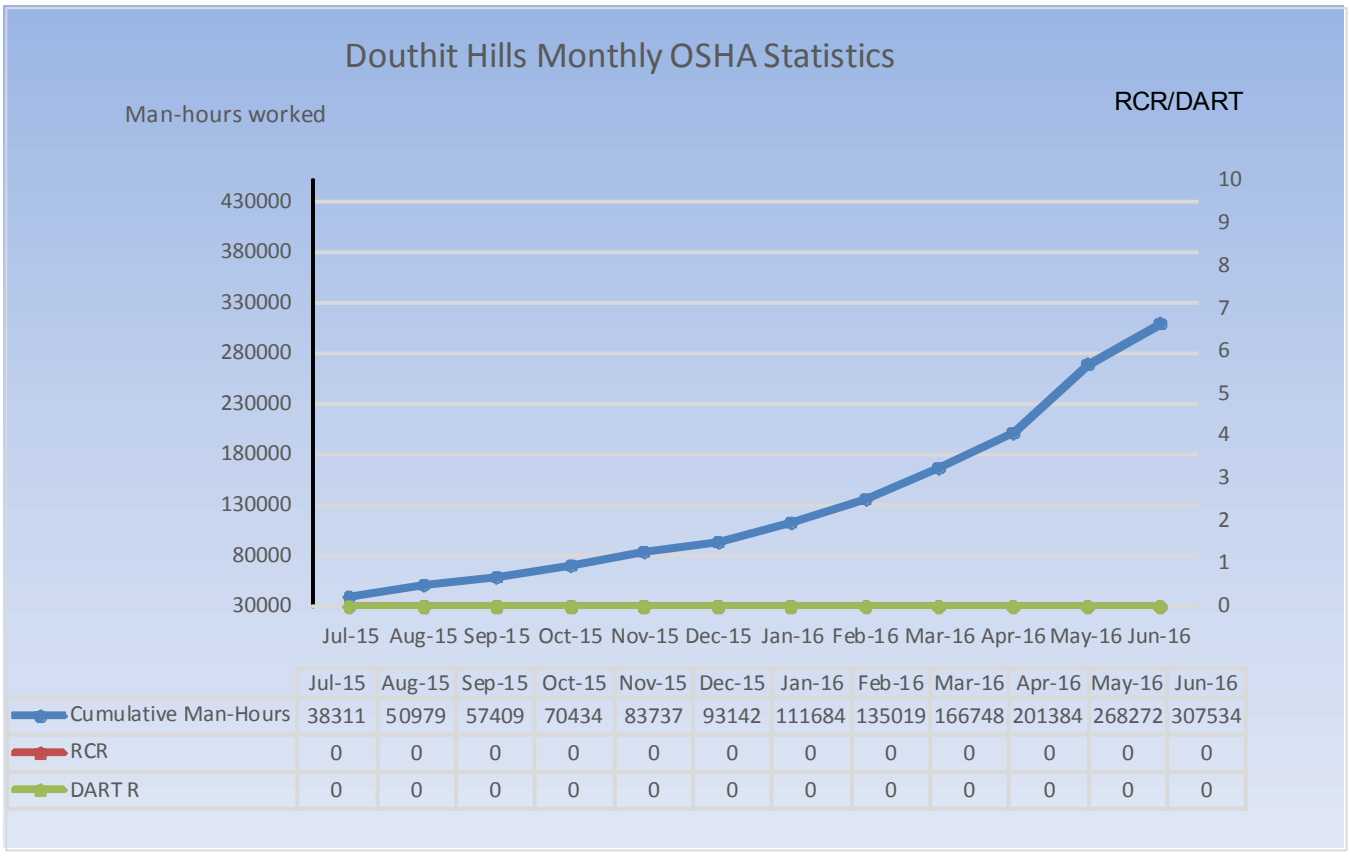

	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16	Jun-16
Cumulative Man-Hours	38311	50979	57409	70434	83737	93142	111684	135019	166748	201384	268272	307534
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART R	0	0	0	0	0	0	0	0	0	0	0	0
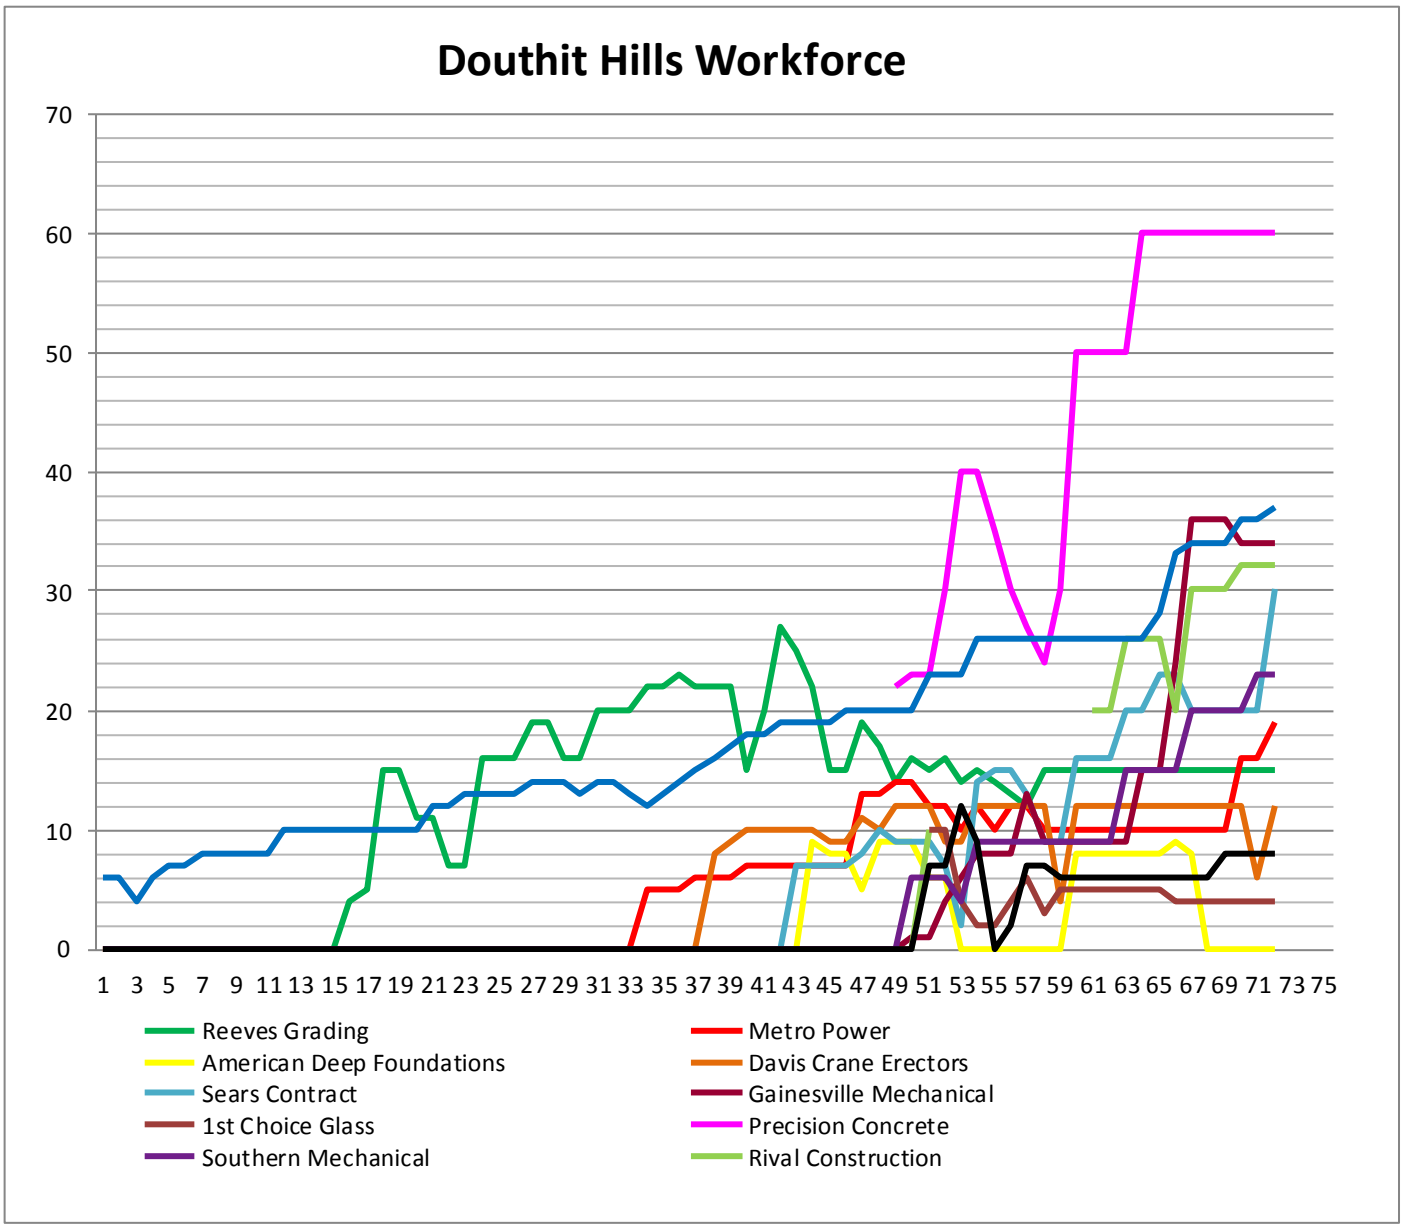
MANPOWER CHART
